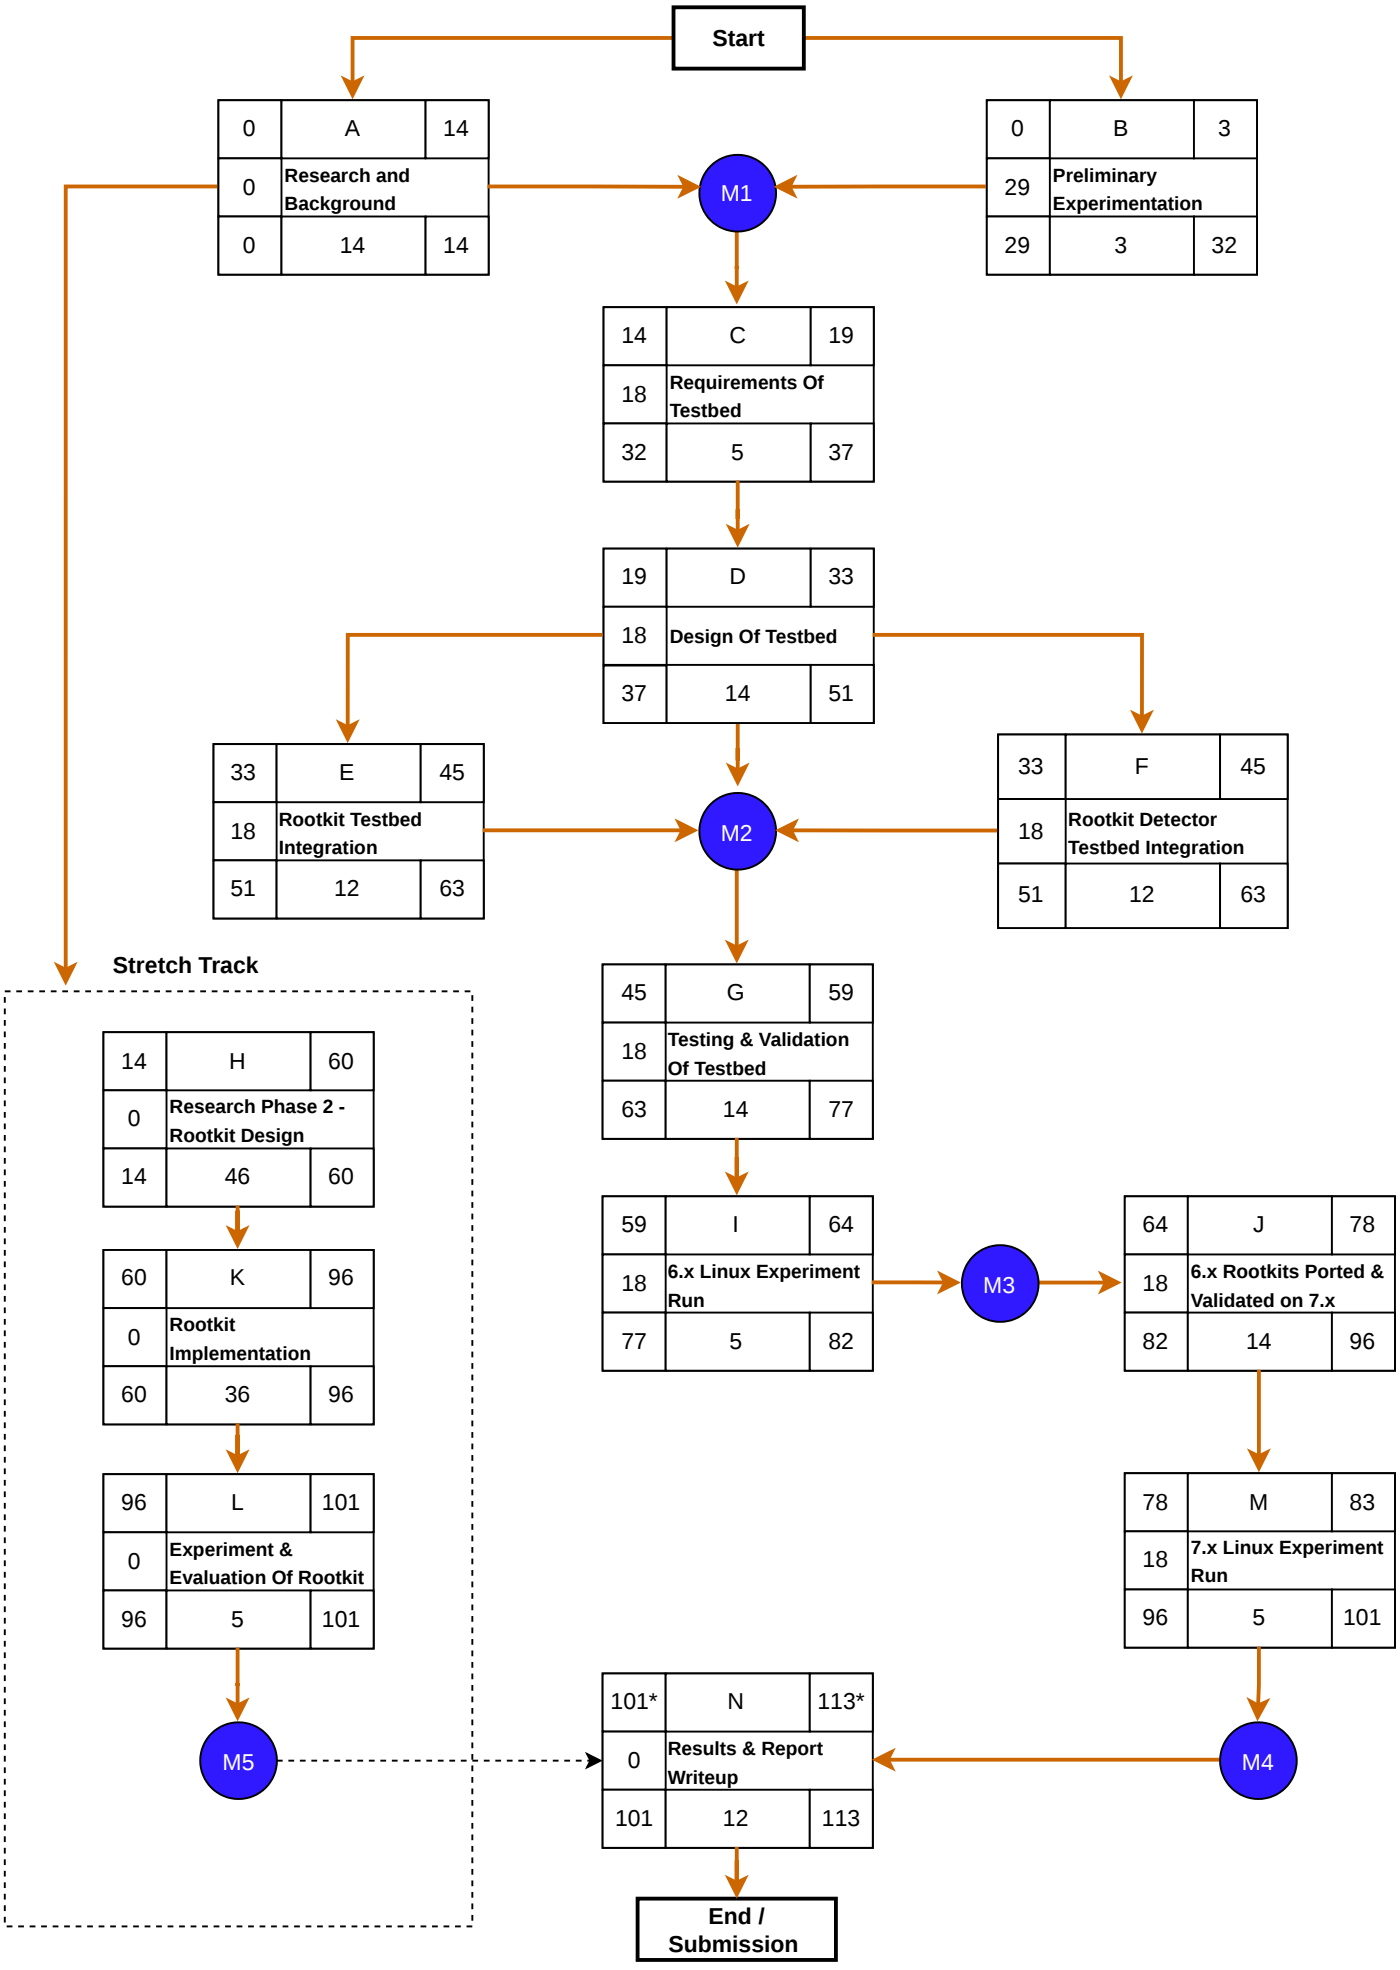

Start
0 | A | 14
0 | Research and Background
0 | 14 | 14
0 | B | 3
29 | Preliminary Experimentation
29 | 3 | 32
M1
14 | C | 19
18 | Requirements Of Testbed
32 | 5 | 37
19 | D | 33
18 | Design Of Testbed
37 | 14 | 51
33 | E | 45
18 | Rootkit Testbed Integration
51 | 12 | 63
33 | F | 45
18 | Rootkit Detector Testbed Integration
51 | 12 | 63
M2
Stretch Track
45 | G | 59
18 | Testing & Validation Of Testbed
63 | 14 | 77
14 | H | 60
0 | Research Phase 2 - Rootkit Design
14 | 46 | 60
59 | I | 64
18 | 6.x Linux Experiment Run
77 | 5 | 82
M3
64 | J | 78
18 | 6.x Rootkits Ported & Validated on 7.x
82 | 14 | 96
60 | K | 96
0 | Rootkit Implementation
60 | 36 | 96
78 | M | 83
18 | 7.x Linux Experiment Run
96 | 5 | 101
96 | L | 101
0 | Experiment & Evaluation Of Rootkit
96 | 5 | 101
M5
M4
101* | N | 113*
0 | Results & Report Writeup
101 | 12 | 113
End / Submission
KEY
Earliest Start | ID | Earliest Finish
Slack | Name
Latest Start | Duration | Latest Finish
= Milestone
= Stretch / Optional
All values are in days

ECSP3000 - Plan & Milestones

Elliott Jelbert ej1g24@soton.ac.uk Supervisor: Dr BooJoong Kang

---

PERT & Gantt Chart

The PERT chart maps out the dependencies of the different tasks & milestones within my project. The values on the graph use an expected time - in days - calculated from the optimistic, most likely and pessimistic time estimates.

The stretch track will be developed in parallel with the rest of the project starting after initial research is complete. A decision will be made after milestone **M3** (Est. January) as to if a complete rootkit design will be pursed, contigent on time & feasibility.

The PERT Expected Time values were then used to produce a Gantt Chart, mapped against calendar months to help better visualise my project's planned progress against milestones & deadlines.

Tasks

ID	Task	O	M	P	TE $= \lceil (O + 4M + P)/6 \rceil$
A	Research & Background	10	15	26	16
B	Preliminary Experimentation	5	8	17	9
C	Requirements of Testbed	7	14	27	15
D	Design of Testbed	20	30	46	31
E	Rootkit Testbed Integration	10	14	24	15
F	Rootkit Detector Testbed Integration	20	28	42	29
G	Testing & Validation of Testbed	3	5	13	6
H	Research Phase 2 - Rootkit Design	3	5	13	6
I	6.x Linux Experiment Run	3	5	13	6
J	6.x Rootkits Ported & Validated on 7.x	3	5	13	6
K	Rootkit Implementation	3	5	13	6
L	Experiment & Evaluation of Rootkit	3	5	13	6
M	7.x Linux Experiment Run	3	5	13	6
N	Results & Report Writeup	3	5	13	6
				Total	**121**

Milestones

These are the milestones I have defined as the major points of progress within my project.

ID	Name	Description	Est. Completed
M1	Research & Feasibility Completed	Finished background research & completed some initial experimentation.	Early-Nov 2026
M2	Testbed & Integration Complete	Testbed design completed & detectors/rootkits integrated.	Mid-Dec 2026
M3	6.x Experiment Data Analysed	Collected & analysed data from the 6.x experiment run.	Mid-Jan 2027
M4	7.x Experiment Data Analysed	Collected & analysed data from the 7.x experiment run.	Mid-Feb 2027
M5	Rootkit Designed & Evaluated **(Stretch)**	Rootkit has been designed, developed and used to evaluate relevant rootkit detectors using the testbed.	Mid-March 2027
