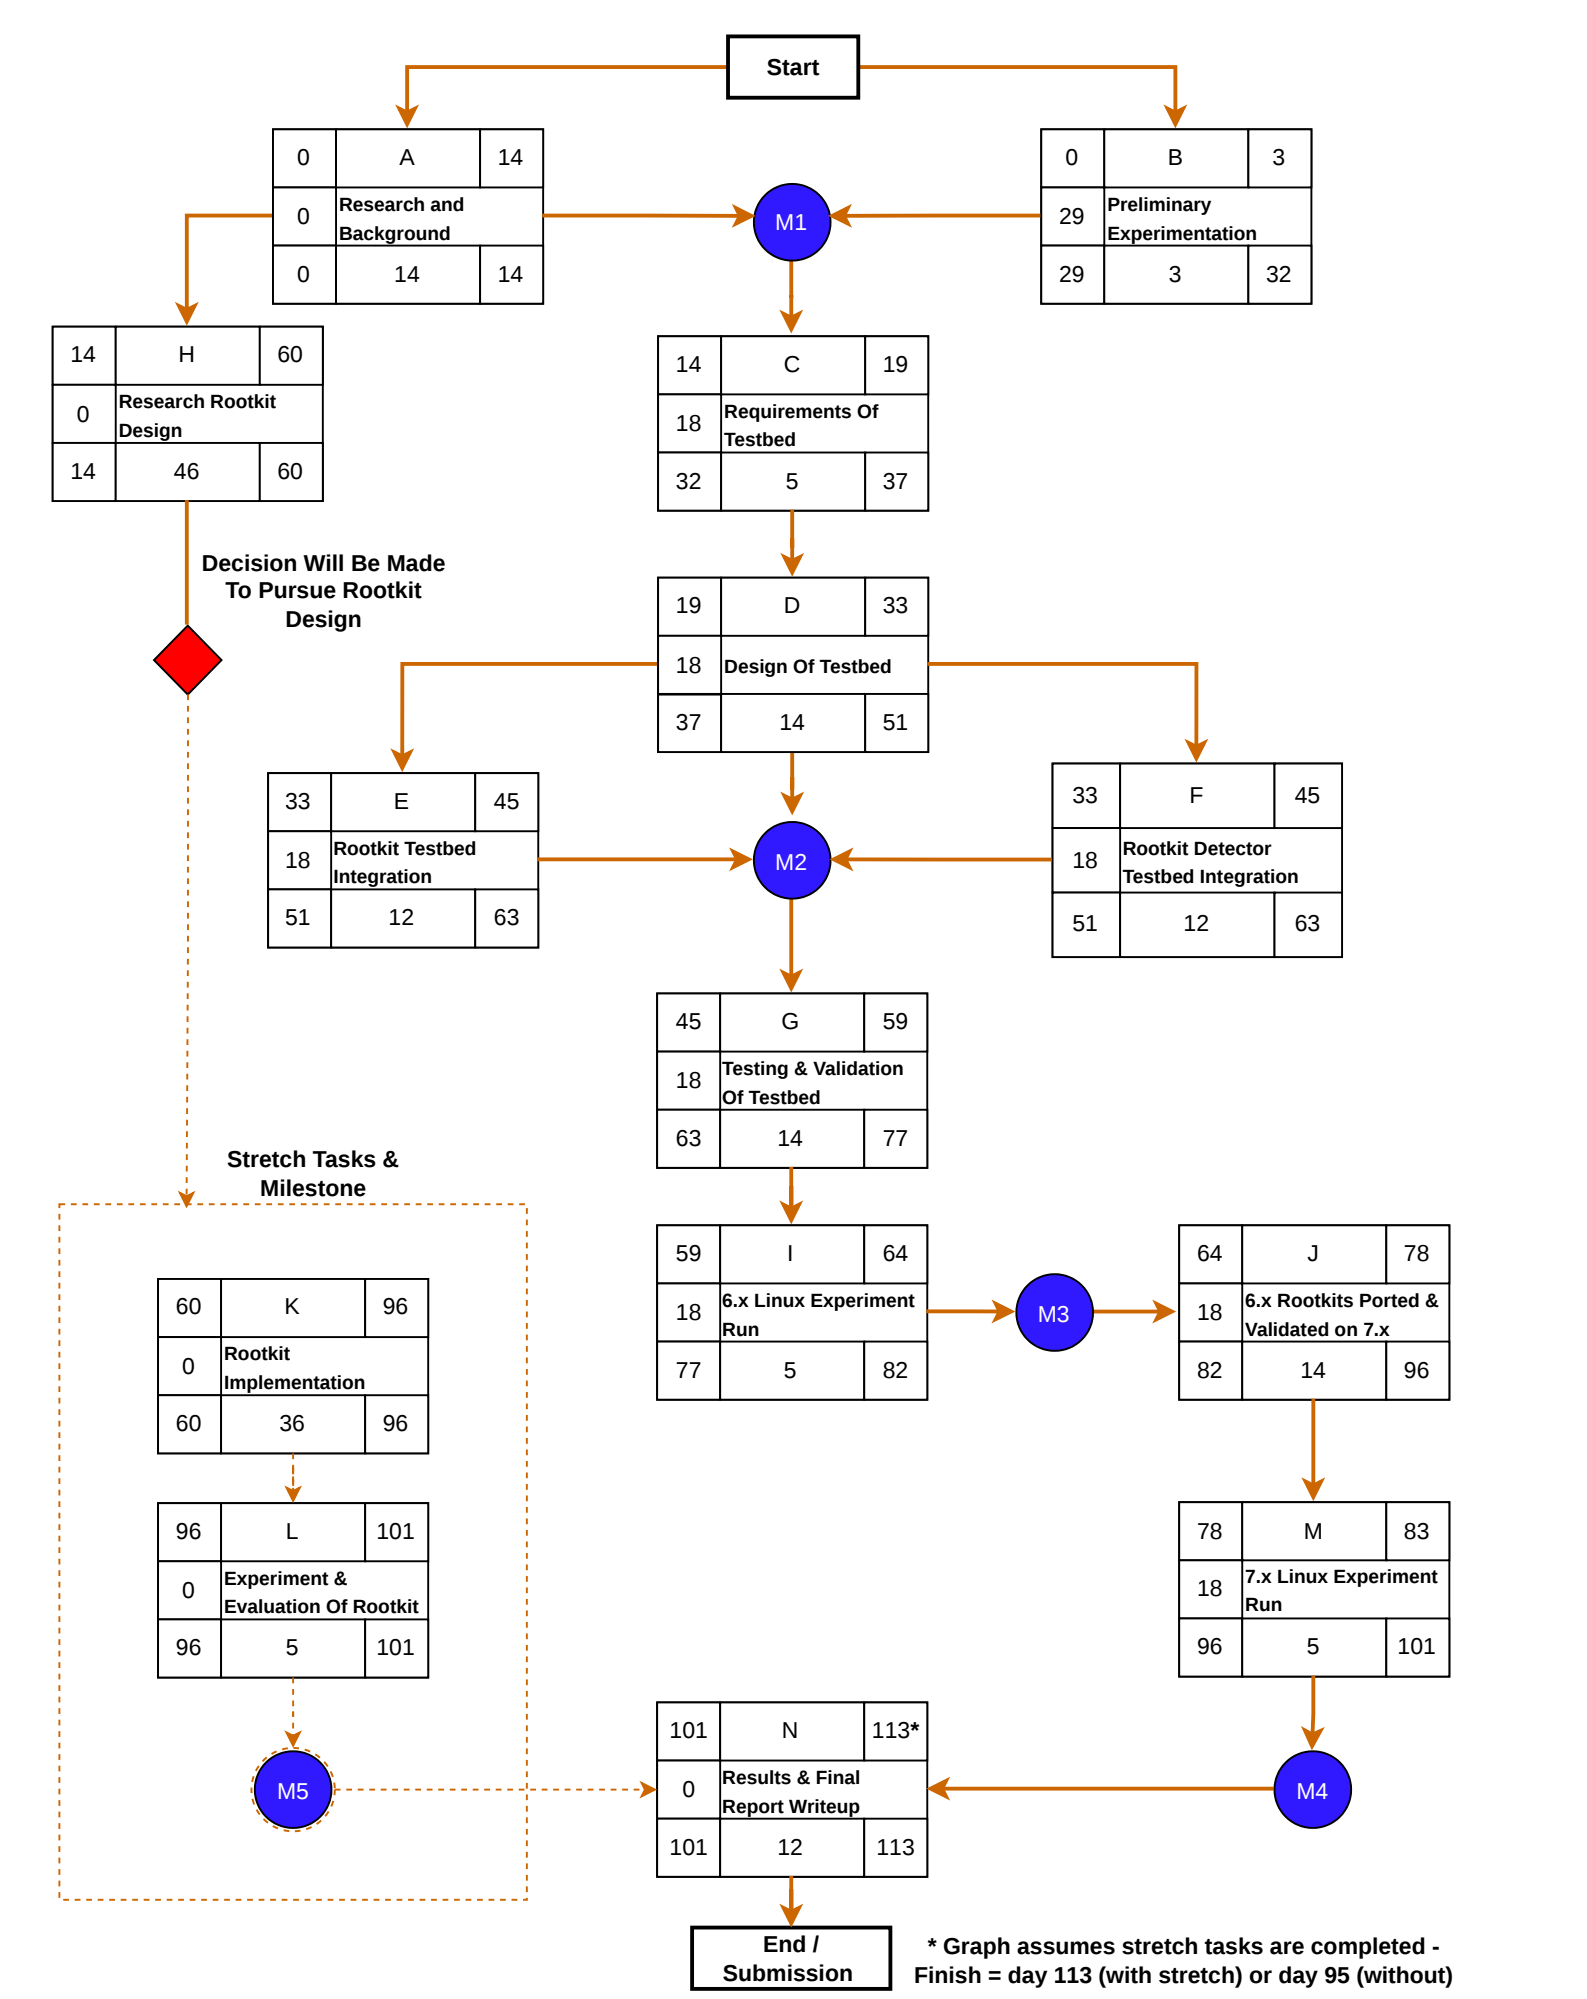

Start
0 A 14
0 Research and Background
0 14 14
0 B 3
29 Preliminary Experimentation
29 3 32
M1
14 H 60
0 Research Rootkit Design
14 46 60
14 C 19
18 Requirements Of Testbed
32 5 37
Decision Will Be Made To Pursue Rootkit Design
19 D 33
18 Design Of Testbed
37 14 51
33 E 45
18 Rootkit Testbed Integration
51 12 63
M2
33 F 45
18 Rootkit Detector Testbed Integration
51 12 63
45 G 59
18 Testing & Validation Of Testbed
63 14 77
Stretch Tasks & Milestone
59 I 64
18 6.x Linux Experiment Run
77 5 82
M3
64 J 78
18 6.x Rootkits Ported & Validated on 7.x
82 14 96
60 K 96
0 Rootkit Implementation
60 36 96
96 L 101
0 Experiment & Evaluation Of Rootkit
96 5 101
78 M 83
18 7.x Linux Experiment Run
96 5 101
M5
101 N 113*
0 Results & Final Report Writeup
101 12 113
M4
End / Submission
* Graph assumes stretch tasks are completed - Finish = day 113 (with stretch) or day 95 (without)
KEY
Earliest Start | ID | Earliest Finish
Slack | Name
Latest Start | Duration | Latest Finish
All values are in days
= Milestone
= Stretch
= Decision Point
