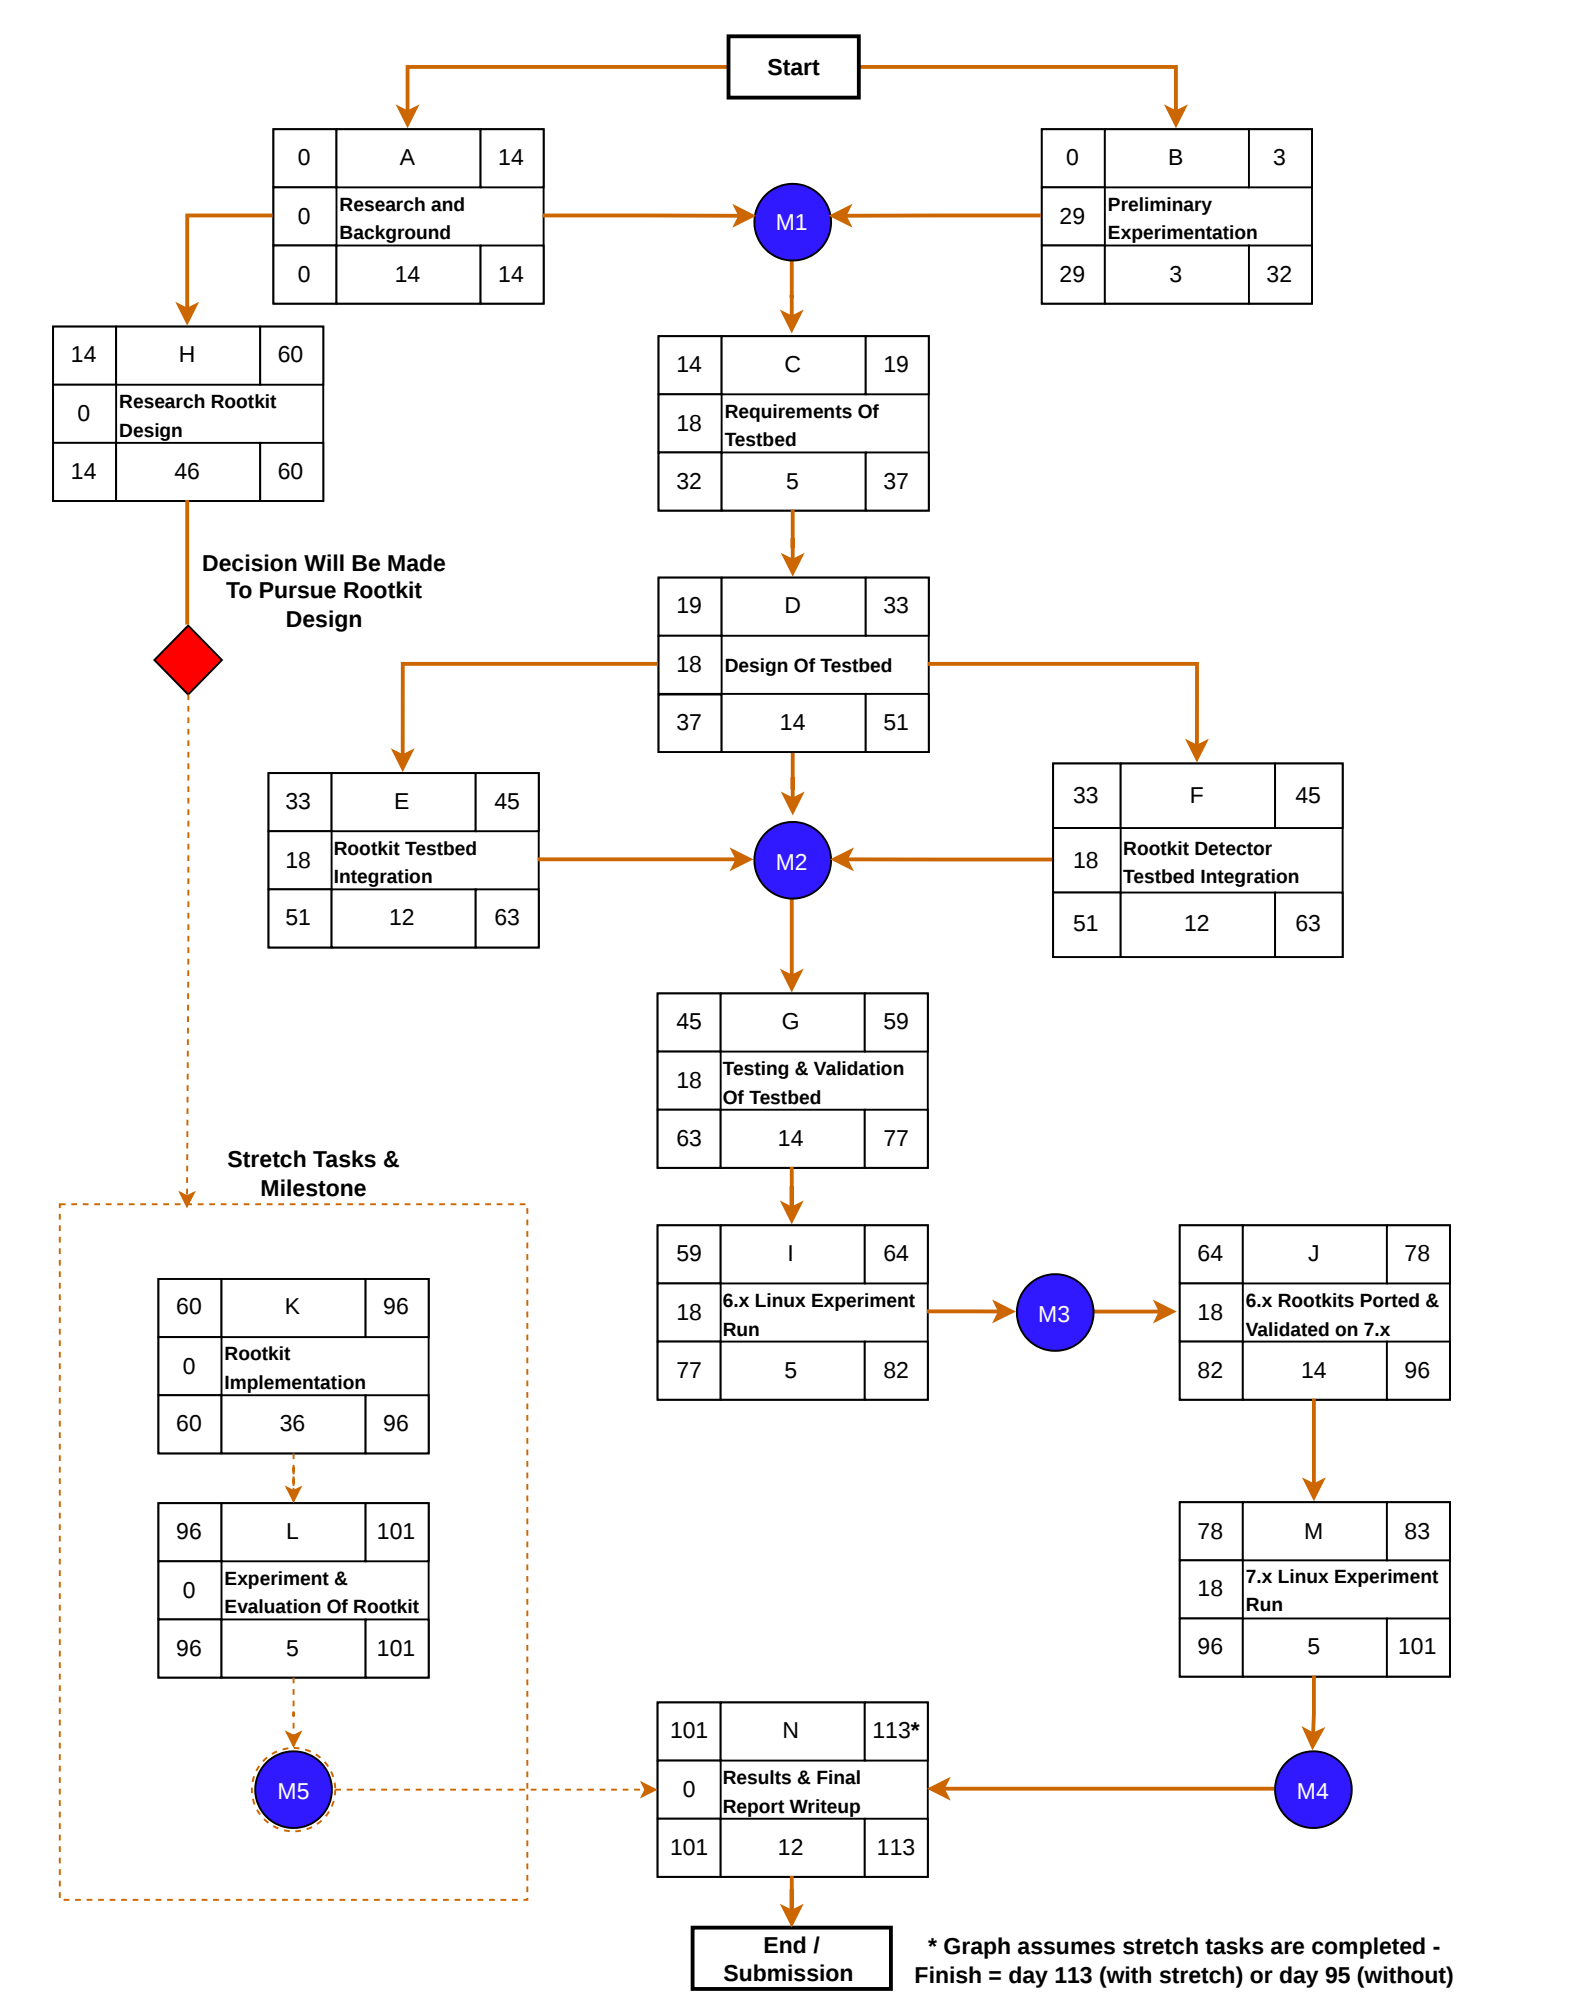

Start
A
Research and Background
B
Preliminary Experimentation
M1
H
Research Rootkit Design
C
Requirements Of Testbed
Decision Will Be Made To Pursue Rootkit Design
D
Design Of Testbed
E
Rootkit Testbed Integration
F
Rootkit Detector Testbed Integration
M2
G
Testing & Validation Of Testbed
Stretch Tasks & Milestone
I
6.x Linux Experiment Run
M3
J
6.x Rootkits Ported & Validated on 7.x
K
Rootkit Implementation
L
Experiment & Evaluation Of Rootkit
M
7.x Linux Experiment Run
M5
M4
N
Results & Final Report Writeup
End / Submission
* Graph assumes stretch tasks are completed - Finish = day 113 (with stretch) or day 95 (without)
KEY
All values are in days
Earliest Start
ID
Earliest Finish
Slack
Name
Latest Start
Duration
Latest Finish
= Milestone
= Stretch
= Decision Point

ECSP3000 - Plan & Milestones

Elliott Jelbert ej1g24@soton.ac.uk Supervisor: Dr BooJoong Kang

---

Project Plan - PERT & Gantt Chart

The PERT chart was used to map out the dependencies of the different tasks & milestones within my project. The values on the graph use an expected time - in days - calculated from the optimistic, most likely and pessimistic time estimates.

The stretch track will be developed in parallel with the rest of the project starting after initial research is complete. A decision will be made after milestone **M3** (Est. January) as to if a complete rootkit design will be pursued, contigent on time & feasibility.

The PERT Expected Time values were then used to produce a Gantt Chart, mapped against calendar months to help better visualise my project's planned progress against deadlines & projected milestones.

Tasks

ID	Task	O	M	P	TE $= \lceil (O + 4M + P)/6 \rceil$
A	Research & Background	7	14	21	14
B	Preliminary Experimentation	2	3	4	3
C	Requirements of Testbed	3	5	7	5
D	Design of Testbed	7	14	18	14
E	Rootkit Testbed Integration	7	12	14	12
F	Rootkit Detector Testbed Integration	7	12	14	12
G	Testing & Validation of Testbed	7	14	17	14
H	Research Phase 2 - Rootkit Design	30	45	65	46
I	6.x Linux Experiment Run	3	4	7	5
J	6.x Rootkits Ported & Validated on 7.x	7	14	21	14
K	Rootkit Implementation	28	36	42	36
L	Experiment & Evaluation of Rootkit	3	4	7	5
M	7.x Linux Experiment Run	3	4	7	5
N	Results & Report Writeup	7	12	14	12
				Total	**197**

Milestones

These are the milestones I have defined as the major points of progress within my project.

ID	Name	Description	Est. Completed
M1	Research & Feasibility Completed	Finished background research & completed some initial experimentation.	Early-Nov 2026
M2	Testbed & Integration Complete	Testbed design completed & detectors/rootkits integrated.	Mid-Dec 2026
M3	6.x Experiment Data Analysed	Collected & analysed data from the 6.x experiment run.	Mid-Jan 2027
M4	7.x Experiment Data Analysed	Collected & analysed data from the 7.x experiment run.	Mid-Feb 2027
M5	Rootkit Designed & Evaluated **(Stretch)**	Rootkit has been designed, developed and used to evaluate relevant rootkit detectors using the testbed.	Mid-March 2027
